

ship July 20

ASAP

Page 1

Work Order ID 149041

149041

Monday, July 18, 2016 1:18:08 PM

Item ID: DSI 9506-011 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Bearpaw Mod - Aerazur Float Compatibility
 Start Date: 7/18/2016 Start Qty: 1.00 *1* Cust Item ID:
 Required Date: 7/20/2016 Req'd Qty: 1.00 *1* Customer:
 Reference:

Approvals: Process Plan: dem Date: 16/07/18 Tooling: _____ Date: _____
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____
 Run Start *NR1*
 Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
DSI 9506	A								
100	Document Control	JUL 18 2016 0.00	DAS 8 9-89					DAS 21 9-89 16-07-18	
100									
DC	Memo	0.00							
Doc.Control -USB or Paperwork	Photocopy bluefile & type labels per PPP DSI 9506-011 CHG001								
110	Pick Kit	0.00							
110									
Packaging	Memo	0.00							
Packaging									
120	QC4- 100% Inspect kits for completeness	0.00							
120									
QC	Memo	0.01							
Quality Control									

JUL 19 2016

JUL 18 2016

JUL 19 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		OTHER : _____					

Work Order ID 149041***149041***

Page 2

Monday, July 18, 2016 1:18:08 PM

Item ID: DSI 9506-011

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Bearpaw Mod - Aerazur Float Compatibility

Start Date: 7/18/2016 Start Qty: 1.00

1

Cust Item ID:

Required Date: 7/20/2016 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start

NR1

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
130		0.00							
130									
Packaging	Memo	0.00							
Packaging	Identify and pack for shipping as per PPP DSI 9506-011 Location: _____ PPP rev: _____								
140	QC21- Final Inspection - Work Order Release	0.00							
140									
QC	Memo	0.02							
Quality Control									

DAS

27

9-89

JUL 19 2016

DAS
21
9-89

JUL 19 2016

Em 16/07/19

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐							
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 			
Description Work Order Deviation				Disposition							
								Completed By			
								Lead hand / Supervisor Approval Verification			
								QC / QA Coordinator Approval			

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER :							
Misidentified	☐	Past Due	☐								

Picklist Print

Monday, July 18, 2016 1:18:08 PM

Page 1

Work Order ID: 149041

149041

Parent Item: DSI 9506-011

DSI 9506-011

Parent Item Name: Bearpaw Mod - Aerazur Float Compatibility

Start Date: 7/18/2016

Required Date: 7/20/2016

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP Rev:A new issue DD 10.03.18 verified by:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

AN4-12A		Purchased	No			110	Each	101.0000	4	4			
---------	--	-----------	----	--	--	-----	------	----------	---	---	--	--	--

AN4-12A

Bolt

DAS
27
9-89

Location	Loc Qty	Loc Code
FG	10	
120423	10	
ST344	91	
m134606	91	

D2274

Manufactured No

D2274

Radius Block

DAS
27
9-89

Location	Loc Qty	Loc Code
FG	12	
86855	12	
ST006	216	
110264	12	
144391	44	
146624	160	
ST012a	303	
147530	303	

D2529

Manufactured No

D2529

Washer

DAS
27
9-89

Location	Loc Qty	Loc Code
ST008	701	
108881	12	
145269	189	
147569	500	

DAS
27
9-89

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

Picklist Print

Monday, July 18, 2016 1:18:08 PM

Page 2

Work Order ID: 149041

149041

Parent Item: DSI 9506-011

DSI 9506-011

Parent Item Name: Bearpaw Mod - Aerazur Float Compatibility

Start Date: 7/18/2016

Required Date: 7/20/2016

Start Qty: 1.00

Required Qty: 1.00

D3171-1

Manufactured No

110

Each

44.0000

4 4

D3171-1

Angle Bracket

DAS
8-09

MS21042L4

Purchased No

110

Each

2,002.000

4 4

MS21042L 4

Locknut

DAS
8-09

Location

Loc Qty

Loc Code

ST019

44

143608

44

Location

Loc Qty

Loc Code

FP001

51

m133363

51

GA

156

m133769

156

OVER007

1000

m135127

1000

ST3003

228

m134955

228

ST303

550

m127376

12

m134861

38

m135058

500

ST305

17

m130922

17

JUL 19 2016

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐								
Misidentified	☐	Past Due	☐	OTHER :							

Picklist Print

Page 3

Monday, July 18, 2016 1:18:08 PM

Work Order ID: 149041

149041

Parent Item: DSI 9506-011

DSI 9506-011

Parent Item Name: Bearpaw Mod - Aerazur Float Compatibility

Start Date: 7/18/2016

Required Date: 7/20/2016

Start Qty: 1.00

Required Qty: 1.00

NAS1149D0463J

Purchased

No

110

Each

2,275.000

4

4

NAS1149D0463.J

WASHER

DAS
●
9-39

JUL 19 2016

DAS
27
9-39

Location

Loc Qty

Loc Code

GA	86	
M132035	21	
M134508	65	
ST260a	2000	
M134943	1000	
M135056	1000	
ST263	189	
M134852	189	

4

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____ Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause				FAULT CATEGORY			
Environment ☐	Design ☐	Doc/Data ☐	Equip/Tooling ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐
Handling/Pre ☐	Material ☐	Internal Transport ☐	Tribal Knowledge ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐
LOA ☐	Substation ☐	Past Expiry Date ☐	Misidentified ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐
				Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐
				Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐
				Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐
				Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐
				Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐
				Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐
				Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐
				OTHER : ☐			

DART SERVICE INSTRUCTION

TO AMEND INSTALLATION INSTRUCTIONS D350-578 REV. F AND EARLIER
AND INSTRUCTIONS FOR CONTINUED AIRWORTHINESS ICA-D350-578 REV. 1 AND EARLIER

REF TCCA STC SH93-4
REF FAA STC SR00028NY
REF FAA STC SR00028NY
REF EASA STC EASA.IM.R.S.01389

TO ENSURE COMPATIBILITY BETWEEN THE D350-578-011/-021 BEARPAW INSTALLATION AND EXISTING AERAZUR FLOAT SYSTEM, CUSTOMERS ARE ENCOURAGED TO PROCURE DSI-9506-011 KIT LISTED BELOW AND PERFORM THE FOLLOWING DEVIATIONS ON INSTALLATION. REFER TO FIGURE 1.

1. MOVE EACH D2432F/D2672F BEARPAW AFT BY 1.50" MAX;
2. SUBSTITUTE AFTMOST D2438 CLAMP WITH TWO D3171-1 ANGLES TRIMMED TO FIT THE AERAZUR FLOAT CLAMPS ON EACH D2432F/D2672F BEARPAW;
3. ADD EXTRA HOLES/COUNTERBORES (Ø0.260" THRU, C'BORE Ø0.930" x 0.300" DEEP FROM BOTTOM) ON EACH D2432F/D2672F BEARPAW TO MOUNT CENTER D2438 CLAMP TO CLEAR AFT CROSSTUBE SADDLE.

IN ALL OTHER RESPECTS, INSTALL THE D350-578-011/-021 BEARPAW INSTALLATION PER INSTALLATION INSTRUCTIONS D350-578 REV. F OR EARLIER.

PARTS LIST

QTY -011	PART NUMBER	DESCRIPTION
X	DSI-9506-011	INSTALLATION MOD KIT
4	D2274	RADIUS BLOCK
4	D2529	WASHER
4	D3171-1	ANGLE
4	AN4-12A	BOLT
4	AN960JD416	WASHER
4	MS21042L4	NUT

CANADA
DEPARTMENT OF TRANSPORT
AIRCRAFT CERTIFICATION
BRANCH
DAO # 01-O-01

APPROVED

BY: 
D. SHEPHERD (DE # 02)

DATE: 10.02.26
CERT. NO.: SH93-4
ISSUE NO.: 7

A	NEW ISSUE	MB	10.02.26
REV.	DESCRIPTION	BY	DATE
DESIGN		DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN			
CHECKED		DRAWING NO.	REV. A
MFG. APPR.	N/A	DSI 9506	SHEET 1 OF 2
APPROVED		TITLE	SCALE
DE APPR.		INSTALL MODIFICATION	NTS
DATE	10.02.26	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

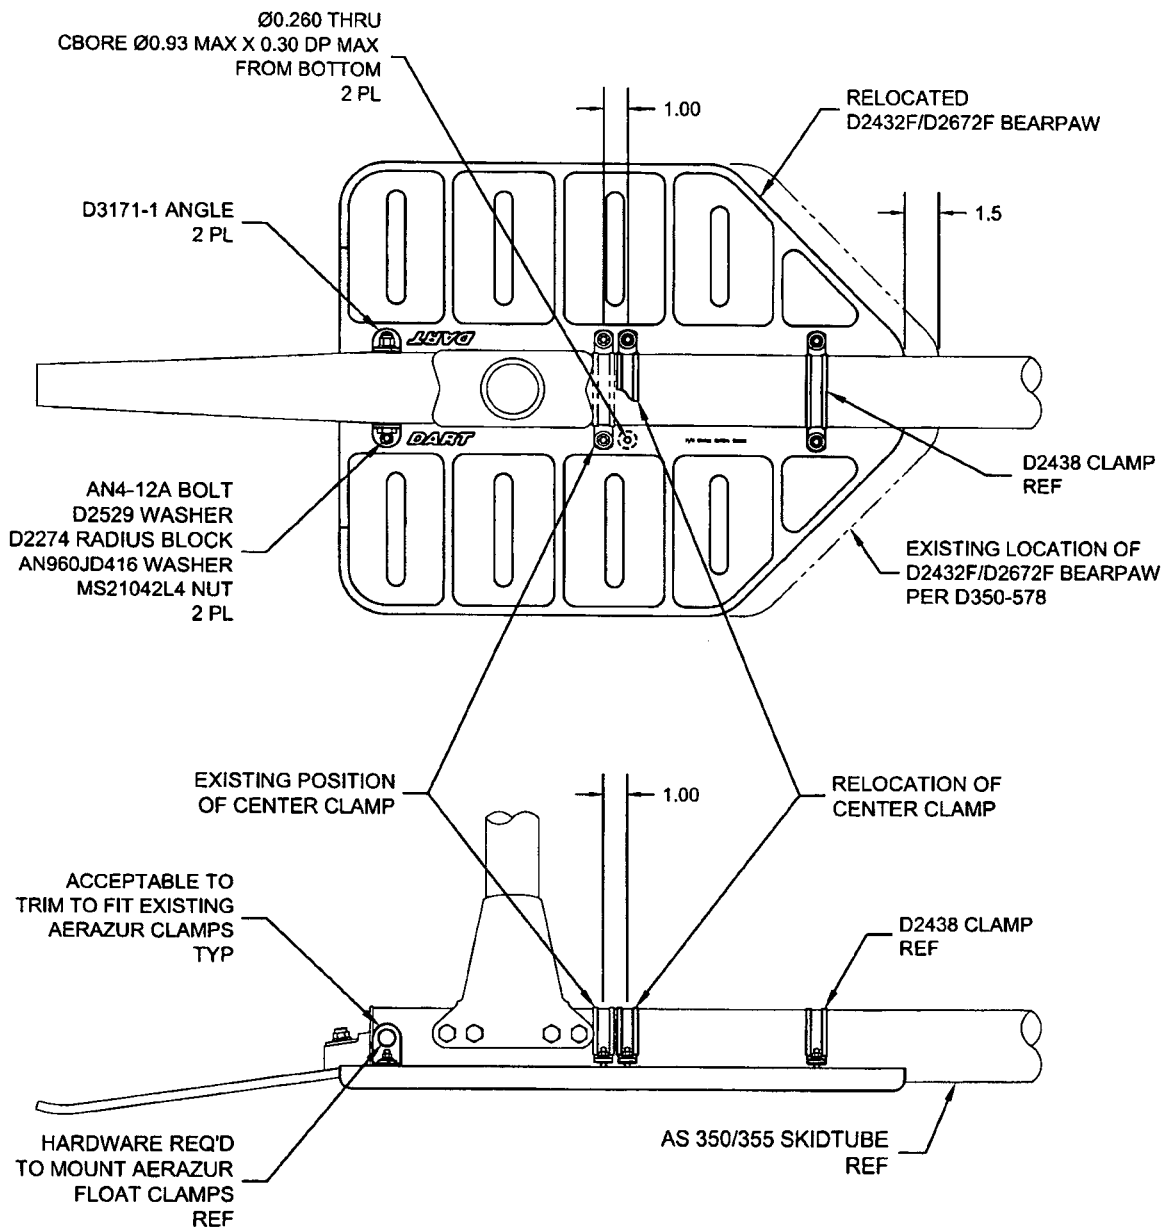


FIGURE 1: INSTALL MOD
(AERAZUR FLOAT AND HARDWARE NOT SHOWN FOR CLARITY)

CANADA
DEPARTMENT OF TRANSPORT
AIRCRAFT CERTIFICATION
BRANCH
DAO # 01-O-01

APPROVED
BY: *[Signature]*
D. SHEPHERD (DE # 02)
DATE: 10.02.26
CERT. NO.: SH93-4
ISSUE NO.: 7

DESIGN		DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN			
CHECKED		DRAWING NO.	REV. A
MFG. APPR.	N/A	DSI 9506	SHEET 2 OF 2
APPROVED		TITLE	SCALE
DE APPR.		INSTALL MODIFICATION	NTS
DATE	10.02.26	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

DART SERVICE INSTRUCTION

TO AMEND INSTALLATION INSTRUCTIONS D350-578 REV. F AND EARLIER
AND INSTRUCTIONS FOR CONTINUED AIRWORTHINESS ICA-D350-578 REV. 1 AND EARLIER

REF TCCA STC SH93-4
REF FAA STC SR00028NY
REF FAA STC SR00028NY
REF EASA STC EASA.IM.R.S.01389

REFERENCE ONLY

TO ENSURE COMPATIBILITY BETWEEN THE D350-578-011/-021 BEARPAW INSTALLATION AND EXISTING AERAZUR FLOAT SYSTEM, CUSTOMERS ARE ENCOURAGED TO PROCURE DSI-9506-011 KIT LISTED BELOW AND PERFORM THE FOLLOWING DEVIATIONS ON INSTALLATION. REFER TO FIGURE 1.

1. MOVE EACH D2432F/D2672F BEARPAW AFT BY 1.50" MAX;
2. SUBSTITUTE AFTMOST D2438 CLAMP WITH TWO D3171-1 ANGLES TRIMMED TO FIT THE AERAZUR FLOAT CLAMPS ON EACH D2432F/D2672F BEARPAW;
3. ADD EXTRA HOLES/COUNTERBORES (Ø0.260" THRU, C'BORE Ø0.930" x 0.300" DEEP FROM BOTTOM) ON EACH D2432F/D2672F BEARPAW TO MOUNT CENTER D2438 CLAMP TO CLEAR AFT CROSSTUBE SADDLE.

IN ALL OTHER RESPECTS, INSTALL THE D350-578-011/-021 BEARPAW INSTALLATION PER INSTALLATION INSTRUCTIONS D350-578 REV. F OR EARLIER.

PARTS LIST

QTY -011	PART NUMBER	DESCRIPTION
X	DSI-9506-011	INSTALLATION MOD KIT
4	D2274	RADIUS BLOCK
4	D2529	WASHER
4	D3171-1	ANGLE
4	AN4-12A	BOLT
4	AN960JD416	WASHER
4	MS21042L4	NUT

CANADA
DEPARTMENT OF TRANSPORT
AIRCRAFT CERTIFICATION
BRANCH
DAO # 01-O-01

APPROVED

BY: 
D. SHEPHERD (DE # 02)

DATE: 10.02.26
CERT. NO.: SH93-4
ISSUE NO.: 7

A	NEW ISSUE	MB	10.02.26
REV.	DESCRIPTION	BY	DATE
DESIGN		DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN			
CHECKED		DRAWING NO.	REV. A
MFG. APPR.	N/A	DSI 9506	SHEET 1 OF 2
APPROVED		TITLE	SCALE
DE APPR.		INSTALL MODIFICATION	NTS
DATE	10.02.26	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
